

---

# VIEWERS' REPORT

—IN—

DITCH PROCEEDINGS.

---

*Elm Ditch  
No 24*

---

No. 680.—Pioneer Press Co., St. Paul, Minn.



*Filed October 13 1894  
J. M. Putnam  
County Auditor*

EXHIBIT 2 OF VIEWERS' REPORT IN DITCH PROCEEDINGS.

Showing Time and Manner in which same must be done. Ditch No. 24

SECTION	TIME WITHIN WHICH WORK MUST BE DONE	MANNER IN WHICH WORK MUST BE DONE	MATERIALS USED	COST OF MATERIALS AND WORK
Stake No. 0 to Stake No. 50	October 28 <sup>th</sup> 1895	Earth removed from ditch along road to the <del>top</del> on level <del>to the</del> <del>ground</del> - elevation to the ground at places on feet from edge of ditch		
Sta 50 to Sta 100	October 10 <sup>th</sup> 1895	Same as above - for bridge at 97 <sup>th</sup> Sta vice 9 <sup>th</sup> plain attached <u>plans</u>		
Sta 100 to 155+60	October 14 <sup>th</sup> 1895	Same as from Sta 0 to Sta 50 Plates on above are all on right hand side of ditch except from 103 to 120 which indicates center of ditch Culvert near 153 above the distance to 14 feet with 14 plain 3" x 12" x 16" with 4 stringers 10" diameter plates on one side with top and ends - base secondary - also with 2 bank piles 12 ft long, 10" diameter and plates in two lines -		

Plan of bridge at Dec 15<sup>o</sup>  
Dunn Pitt no 24

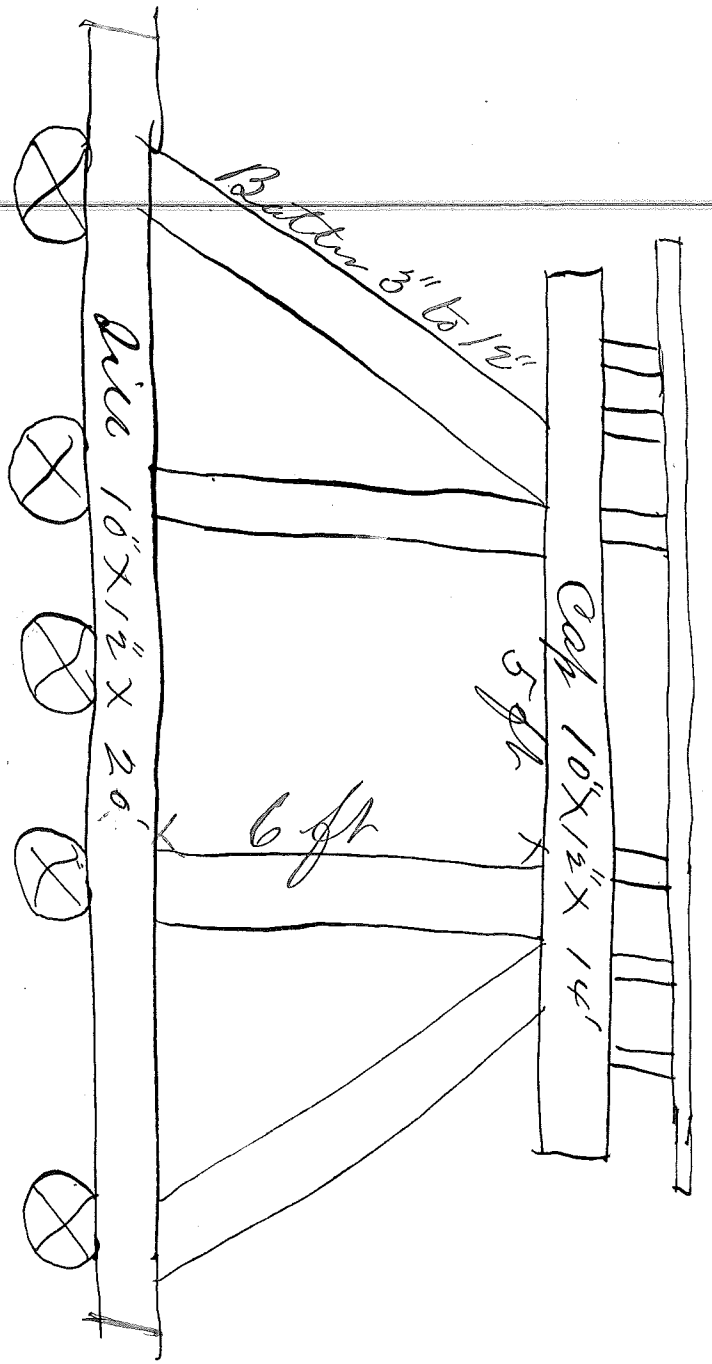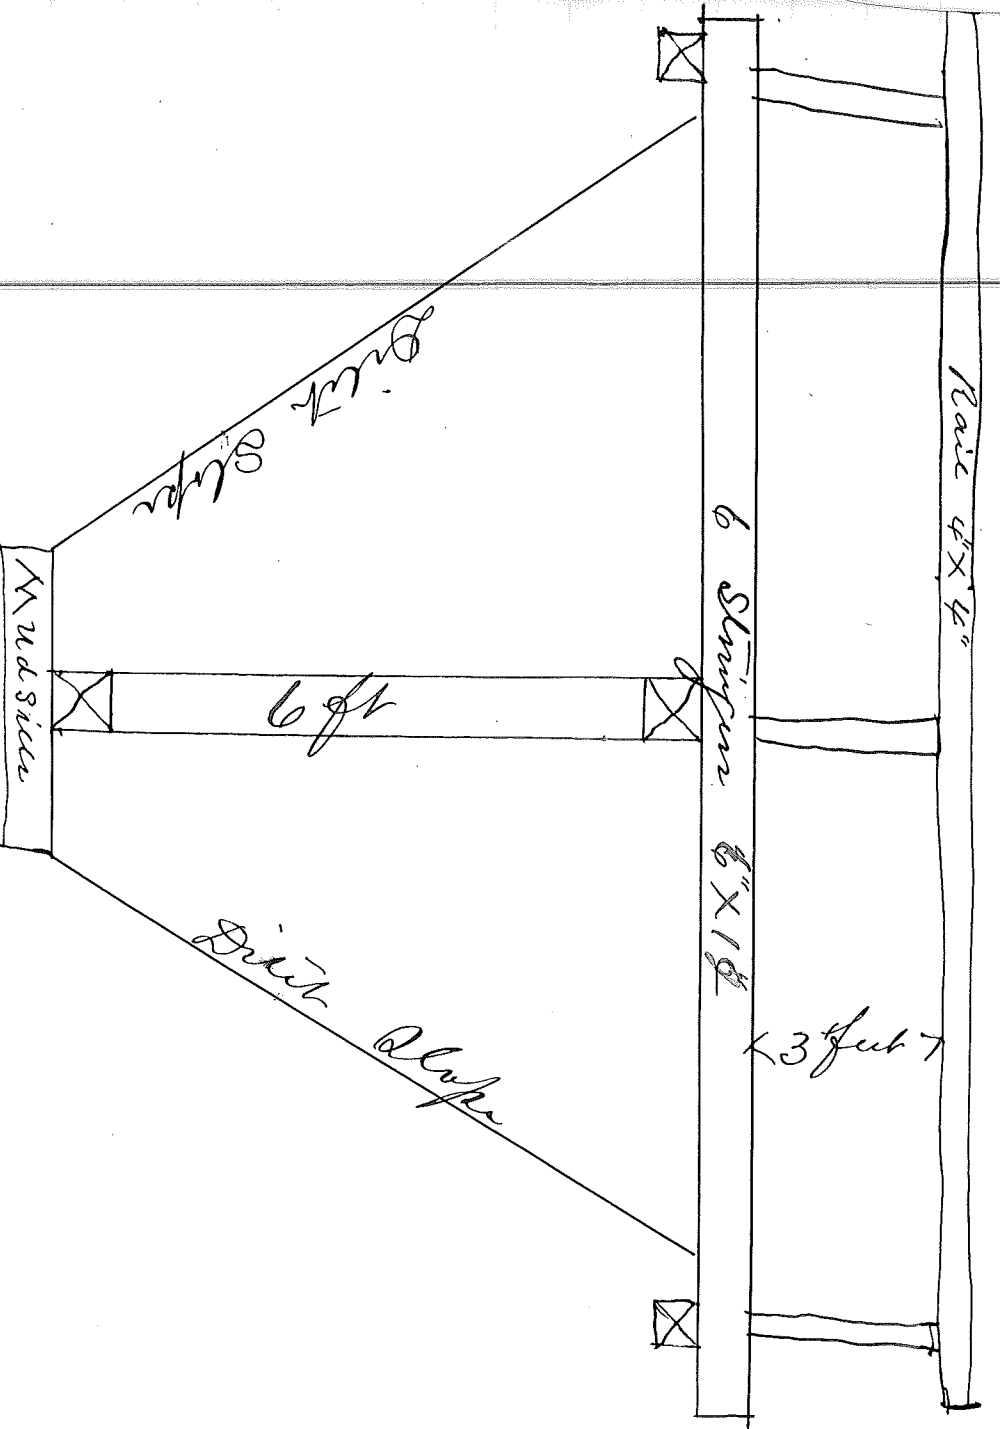

Small Bill No 24

Bill of materials for bridge

at No 99 -

26 planks 3" x 12" x 16'	=	1248	\$
12 stringers 6" x 12" x 14'		1008	"
1 cap 10" x 12" x 14'		140	"
1 bill 10" x 12" x 20		200	"
4 posts 10 x 12 x 8		320	"
2 rails 4 x 4 x 28		65	"
6 posts 4 x 4 x 13		24	"
		<u>3005</u>	"

3005 ft @ 15<sup>00</sup> = 45<sup>00</sup>

5 mens 10' dia iron plates 20 in 5' long } 300

2 hand bills 10' " " 14 " "

30 drift bolts 1/2" x 20" } 80 lbs @ 2<sup>00</sup> = 16<sup>00</sup>

182-6" spikes

Carpenter work 8<sup>00</sup>

Aluminals

3005 feet lumber @ 15<sup>00</sup> 45<sup>00</sup>

Iron stand rails 3.00

Iron work 1.60

Carpenter work etc 8.00

total = \$57.60
