


SEC. 17, T. 31N., R. 24W.

STA. 974 + 00 LT. (F) INP. 15" x 24" C.M.P. REMOVE 24' LIN. FT.
 STA. 974 + 00 LT. (F) INSTALL 15" x 24" C.M.P. F & I 2' METAL APRONS
 STA. 977 + 60 LT. (F) INP. 15" x 24" C.M.P. REMOVE 24' LIN. FT.
 STA. 978 + 27 RT. (F) INSTALL 15" x 24" C.M.P. F & I 2' METAL APRONS
 STA. 979 + 95 RT. (F) INP. 15" x 24" C.M.P. REMOVE 24' LIN. FT.
 STA. 991 + 80 RT. (F) INP. 15" x 24" C.M.P. REMOVE 24' LIN. FT.
 STA. 993 + 83 RT. (F) INSTALL 15" x 24" C.M.P. F & I 2' METAL APRONS

STA. 974 + 62 RT. (F) INP. 15" x 24" C.M.P. REMOVE 24' LIN. FT.
 STA. 977 + 12 LT. (F) INSTALL 18" x 26" C.M.P. F & I 2' METAL APRONS
 STA. 978 + 18 RT. (F) INP. 15" x 24" C.M.P. REMOVE 24' LIN. FT.
 STA. 981 + 50 RT. (F) INP. 18" x 24" C.M.P. REMOVE 24' LIN. FT.

STA. 985 + 74 E. (F) INP. 24" x 56" S.C.P. EXTEND 20' LT. & 4' RT. F & I 2' x 24" S.C.P. F & I 2' CONC. APRONS. EXC. 5.9 CU. YDS.

STA. 975 + 95 LT. (F) INP. 15" x 24" C.M.P. REMOVE 24' LIN. FT.
 STA. 975 + 00 TO STA. 975 + 25 LT. (F) ADDITIONAL SUBCUT 3.0' DEPTH. SEE SHEET NO. 3 SECTION NO. 2 TYPICAL SECTION.

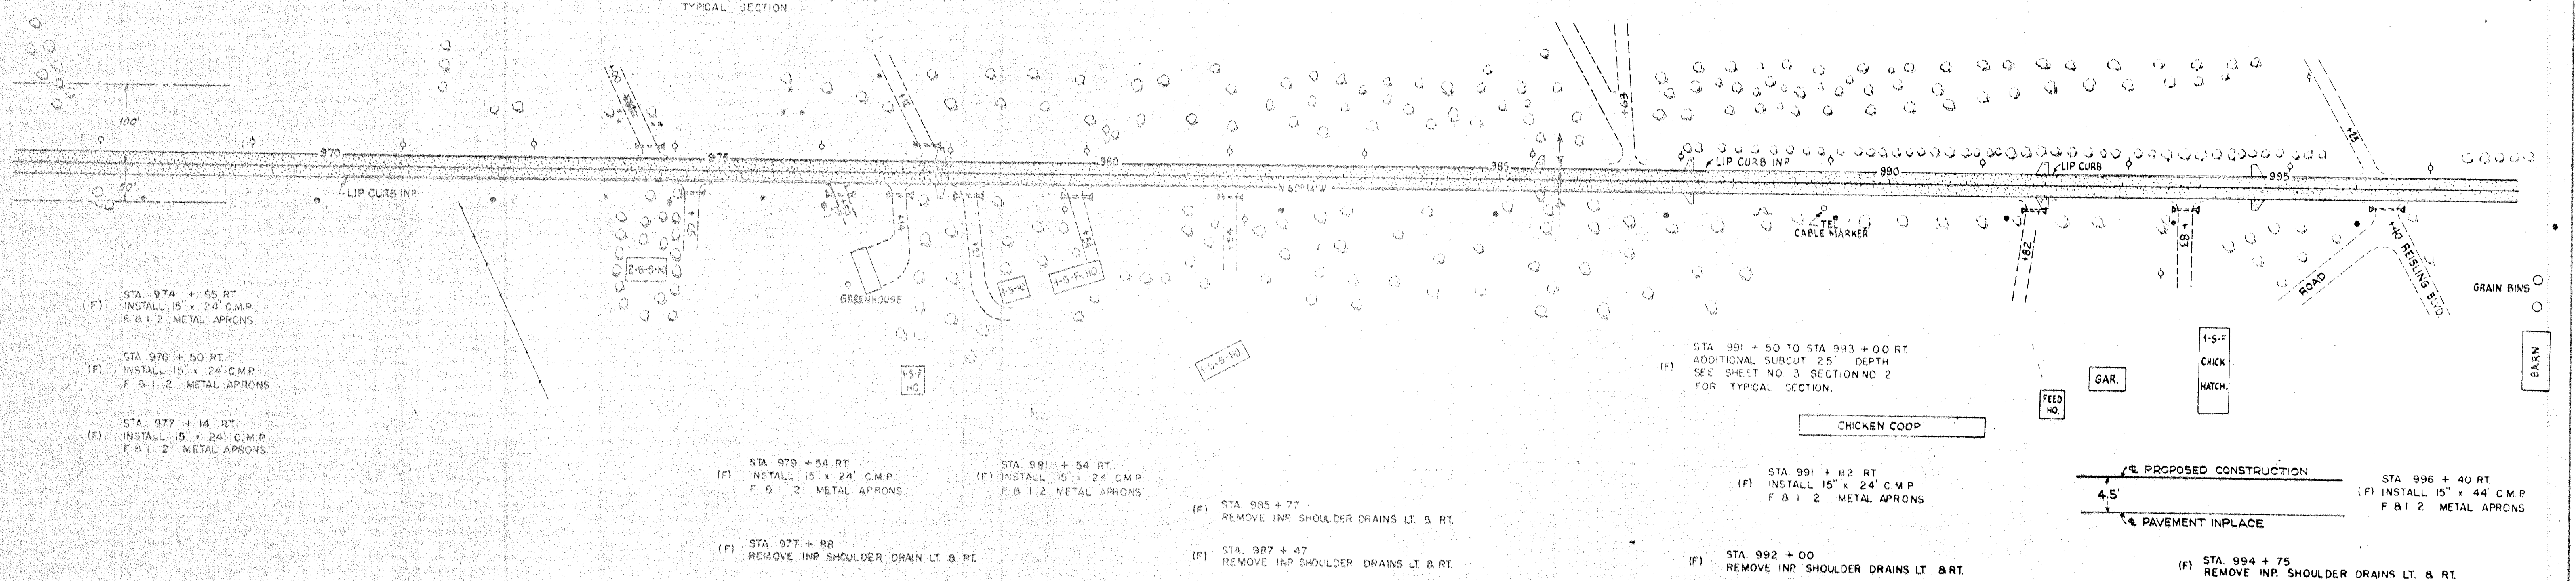

STA. 974 + 65 RT. (F) INSTALL 15" x 24" C.M.P. F & I 2' METAL APRONS
 STA. 976 + 50 RT. (F) INSTALL 15" x 24" C.M.P. F & I 2' METAL APRONS
 STA. 977 + 14 RT. (F) INSTALL 15" x 24" C.M.P. F & I 2' METAL APRONS

STA. 979 + 54 RT. (F) INSTALL 15" x 24" C.M.P. F & I 2' METAL APRONS
 STA. 981 + 54 RT. (F) INSTALL 15" x 24" C.M.P. F & I 2' METAL APRONS

STA. 985 + 77 (F) REMOVE INP. SHOULDER DRAINS LT. & RT.
 STA. 987 + 47 (F) REMOVE INP. SHOULDER DRAINS LT. & RT.

STA. 991 + 50 TO STA. 993 + 00 RT. (F) ADDITIONAL SUBCUT 2.5' DEPTH. SEE SHEET NO. 3 SECTION NO. 2 FOR TYPICAL SECTION.

STA. 991 + 12 RT. (F) INSTALL 15" x 24" C.M.P. F & I 2' METAL APRONS

STA. 992 + 00 (F) REMOVE INP. SHOULDER DRAINS LT. & RT.

STA. 994 + 75 (F) REMOVE INP. SHOULDER DRAINS LT. & RT.

STA. 996 + 40 RT. (F) INSTALL 15" x 44" C.M.P. F & I 2' METAL APRONS

B.M. ELEV. 876.10
 SPIKE IN 26" BOXELDER
 45' RT. STA. 954+03



(F) 20 CL. 9 TREES L/R
 (F) 39 GR. 9 TREES L/R
 (F) 0.00 ACRE RT.
 (F) 0.00 ACRE RT.
 (F) 0.70 ACRE LT.
 (F) 0.70 ACRE LT.
 (F) 77 CL. 4 TREES L/R
 (F) 130 GR. 4 TREES L/R
